Hugo Modernisation Scrum Ceremonies and Sprint Process

Agile Ceremonies in Bupa

Scrum Ceremony	Description	Timeframe
Backlog Refinement	A meeting to review and prioritize the product backlog.	This will need to be 2 weeks ahead of the sprint planning session and occurs every fortnight.
Sprint Planning	A meeting to plan the upcoming sprint and prioritize the backlog.	This happens the day before the sprint starts or the first day of the sprint every fortnight. Stories elaborated with acceptance criteria and ready to GO
Daily Scrum	A daily team meeting where the team members discuss what they have accomplished , what they are working on and any blockers.	Scheduled daily for a duration of 15 -30 mins.
Sprint Review	A review of the completed work during the sprint and the demo to the stakeholders.	This meeting will be scheduled for the last day of the sprint every fortnight.
Sprint Retrospective	A meeting to reflect on the previous sprint and identify the areas of improvement.	This meeting will be scheduled after every sprint is completed every fortnight/ monthly combining 2 sprints.

Story Points Estimation using Fibonacci

Example	Story Points	Effort Required	Complexity	Risk and Uncertainties
No work needed	1	Low	Low	Low
Very trivial tasks like changing a label	2	Medium-Low	Low	Medium-Low
Simple bug fixes	3	Medium	Medium	Medium
Minor feature updates	5	Medium-High	Medium-High	High
Implementing Login Screen	8	High	High	High
Adding a basic search functionality	13	Very High	High	Medium-High
Creating User Dashboard	21	Extremely High	Very High	Extremely High

Sprint Process:

Scrum:

Scrum is a well-known Agile project management framework many businesses use to improve productivity and collaboration. At the heart of Scrum are its five ceremonies, named:

•Sprint planning

•Daily Scrum

•Sprint review

•Sprint retrospective

•Backlog refinement

During the sprint planning ceremony, the team decides what they will accomplish during the upcoming sprint. The daily Scrum allows team members to share updates and identify any blockers. The sprint review enables the team to showcase their completed work to stakeholders. And the sprint retrospective is a time for reflection and identification of areas for improvement.

In short, Scrum ceremonies help to promote transparency, collaboration, and communication, all of which are essential for the success of the project.

The Backlog Refinement Ceremony :

The product backlog refinement ceremony aims to refine and prioritize the product backlog for upcoming sprints.

During the backlog refinement ceremony, the entire Scrum team reviews the product backlog items. This is so they can assess their value and priority.

They may add new items, remove outdated ones, or break down larger items into smaller, more manageable tasks. This process helps ensure that the backlog is always up-to-date. And that it contains the most valuable and relevant work items for the upcoming sprints.

Product backlog refinement can also be used to ensure that the team is prepared for future sprints and that everyone is on the same page regarding project goals and priorities. By refining the backlog, the team can maximize their efficiency and focus on delivering value to the customer.

Sprint Planning:

The team collaborates during the sprint planning ceremony to identify and prioritize tasks. The Scrum Master facilitates the meeting, and the entire team, including the product owner, BA , developers, and other stakeholders, should participate. The goal is to have a shared understanding of what needs to be done during the sprint and to set realistic goals for the team.

The sprint planning meeting starts with a review of the product backlog, where the team works together to prioritize and refine items. The team then estimates the work involved in completing the tasks, breaking them into smaller, more manageable tasks.

The team also identifies potential obstacles or dependencies affecting the sprint goals. By the end of the meeting, the Scrum team should have a clear plan and a set of goals for the upcoming sprint cycle.

Daily Scrum:

The daily Scrum or “daily standup” ceremony is about keeping everyone on the same page by reviewing progress and planning for the day ahead. It's a brief meeting every working day of the sprint and typically lasts up to 15 minutes.

All Scrum team members, including the Scrum master, developers, BA and product owner, should attend the daily Scrum. However, it's not limited to these members, as the team can benefit from anyone's input. During the daily Scrum, team members share updates on their work and any obstacles that might be in their way. This review allows everyone to stay up-to-date on progress, identify potential issues, and adjust as needed.

Sprint Review:

During this meeting, the Scrum team demonstrates the work they've completed during the sprint. They also wait for and work on feedback from stakeholders.

The team also reviews the product backlog and discusses what tasks should be prioritized for the next sprint.

The sprint review allows the team to identify any issues or challenges that need to be addressed before the start of the next sprint.

Sprint Retrospective:

The sprint retrospective meeting is held at the end of the sprint. It is an opportunity for the team to reflect on the sprint and identify opportunities for process improvement.

The main goal is to figure out what went well and what didn't and how the team can work together more in the future toward a more successful sprint.

During the retrospective, team members share their thoughts and opinions openly and honestly about the sprint. At the same time, the Scrum master facilitates the discussion and helps the team come up with action items for improvement.

Roles and Responsibilities

- All the product backlogs need to be loaded into ADO in the defined structure of EPIC, FEATURE,USER STORIES by the Business Analyst.
- As a part of the Backlog refinement process the product backlogs are prioritised by the PO along with the Dev lead and BA and the BA refines and elaborates those user stories with acceptance criteria's and assigns sprints. In this meeting BA might add new items, remove outdated ones, or break down larger items into smaller, more manageable tasks. This is also scheduled and facilitated by the Scrum Master. This will need to be 2 weeks ahead of the sprint planning session. All integration impacts and upstream and downstream impacts needs to be documented.
- As a part of the sprint planning meeting, it starts with a review of the product backlog, where the team works together to prioritize and refine items. The team then estimates the work involved in completing the tasks, breaking them into smaller, more manageable tasks for that sprint. This happens the day before the sprint starts or the first day of the sprint. Scrum Master facilitates the meeting along with the BA and BA to input and update ADO.
- All Scrum team members, including the Scrum master, developers and BA should attend the daily Scrum. However, it's not limited to these members, as the team can benefit from anyone's input. During the daily Scrum, team members share updates on their work and any obstacles that might be in their way. This is facilitated by the Scrum Master.

- Sprint Review is facilitated by the Scrum Master and scheduled around the last day of the Sprint to showcase the development done on that sprint and take feedback from the Product Owner. BA, Development lead, development team along with testers and Scrum master the entire team is expected to be present. Any feedback or new requirements are captured in the session and added to the backlog for prioritisation.
- Sprint Retrospective is another ceremony facilitated by the Scrum master to document what went well and how we can improve and implement the learnings from the current/previous sprints into future sprint.
- Dev team should not start the build of a user story until the user story is elaborated and acceptance criteria are defined. Acceptance criteria will be defined by the BA along with the Dev lead, Designer and sent to PO for review and endorsement. This will need to happen as a apart of backlog refinement. Once it is endorsed it can be a candidate for the sprint planning.
- Risks/Issues/Dependencies all needs to be captured in ADO by the Scrum Master and there needs to be a monthly scheduled meeting for going through those RAID items with the whole team.
- Testing team needs to be a part of the whole discussion on all sessions of backlog refinement and sprint planning so that they can understand the integration impacts and have all teams engaged for testing.

HUGO Implementation Timelines

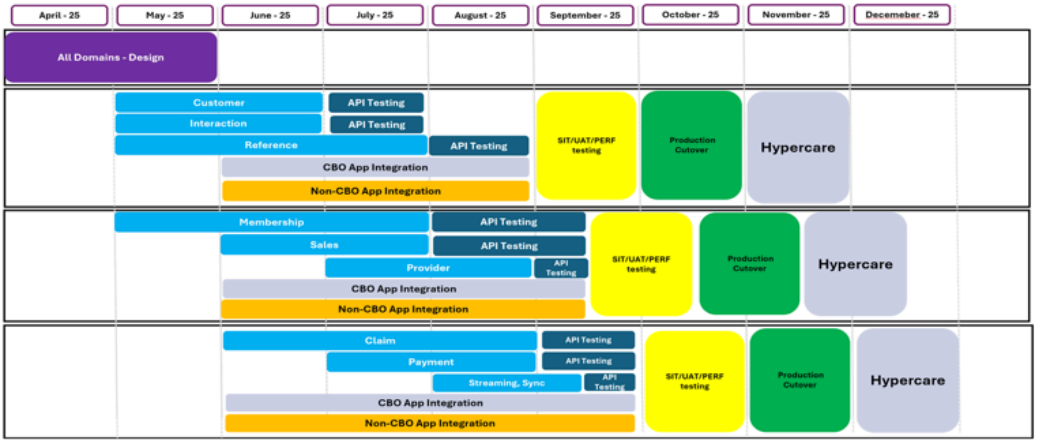

Target Dates Suggestion based on the Milestones shared

- Customer, Interaction, Reference, Membership API functional requirements needs to be documented in Confluence before 31st March.
- Discovery workshops to discuss on all integration scenarios,upstream,downstream impacts should be done by 31st March for the above-mentioned API's.

- As a part of the Design phase completion all the above-mentioned API design should be fully completed before 15th April.
- ADO should be loaded with all the backlog items for these APIs by 15th April.
- Backlog refinement sessions to commence from 15th April to ensure that these stories are prioritised and refined with all acceptance criteria elaborated so that they are all ready for the sprint planning session before 1 May.
- All stories must be having story points and maximum effort for a story can be 13 points which can be completed in a sprint. Anything bigger than that needs to be broken into smaller tasks.
- Inputs to elaborate should be from Dev lead from Hexaware along with product expert, Solution architect and subject matter expert.
- The Sprints in BUPA starts on a Wednesday and ends in a fortnight Wednesday. So ideally the build needs to start from 23 April as a part of 2509 Sprint (23 Apr – 6 May) or commence as a part of 2510 Sprint starting on 7 May.
- Sprint planning needs to be completed a week prior to the Sprint commencement for every sprint.

Technical Debt

Decision	Decision taken by	Implication
No Code Coverage	Anbarasan Rajangam	Code Coverage needs to be added to SOW and costed for the Hugo Implementation Phase.
